Initial Blower Door Test (Depressurize)

Channel A: Input open to house, reference to outside and establish 50 Pascals difference.

Channel B: Input to fan tap, reference to inside, record fan pressure in Pascals and whole house CFM 50.

Notes

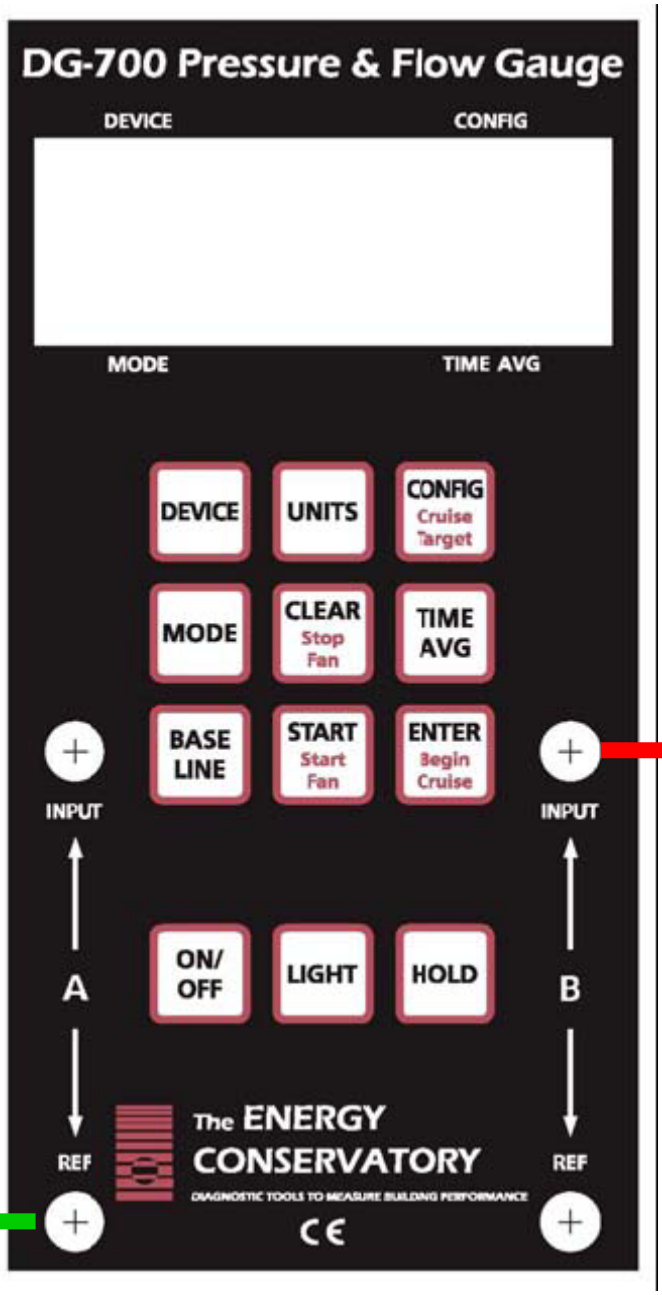

To Fan

To outside

©SWBSTC/FSL-Home Imp. 2016
